



LETU Athletic & Human Performance Air Dome Project

Construction Progress Report

06.04.26

Report Summary:

- Society Drive Expansion underway
- Exterior Landscaping & Irrigation in progress
- Dome Equipment Installation



Progress Report:

Earthwork/Civil:

- Weller / Society Drives asphalt in progress.
- Landscaping nearly complete.

Lobby Building:

- Flooring and finishes nearing completion.
- A/V scope nearing completion.
- I/T scope (LETU) nearing completion.



Progress Report:



Athletic & Human Performance Buildings (Units B & C):

- Telescoping bleachers in progress
- Graphics and signage underway
- Flooring nearly complete
- Furniture installation in progress

Fire Pump House

- Fire Protection and Fire Alarms/Detection/Notification scopes nearing completion.



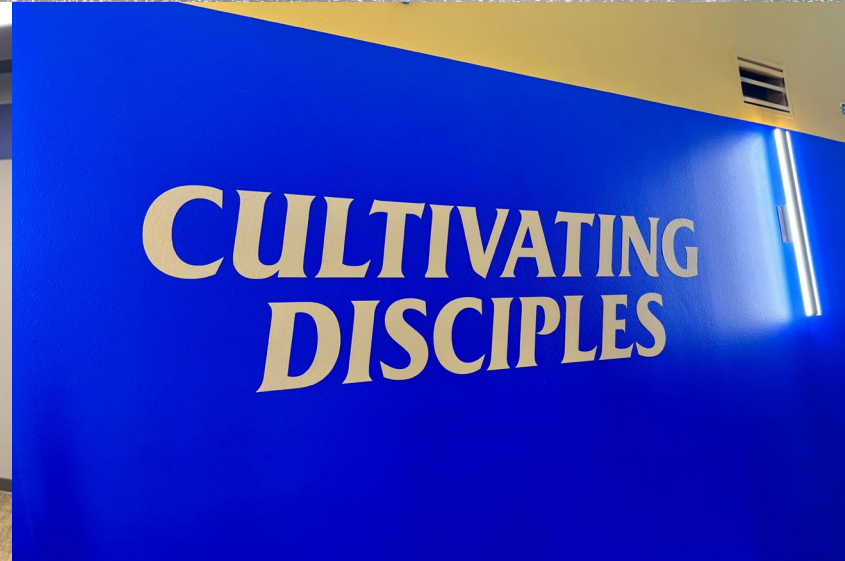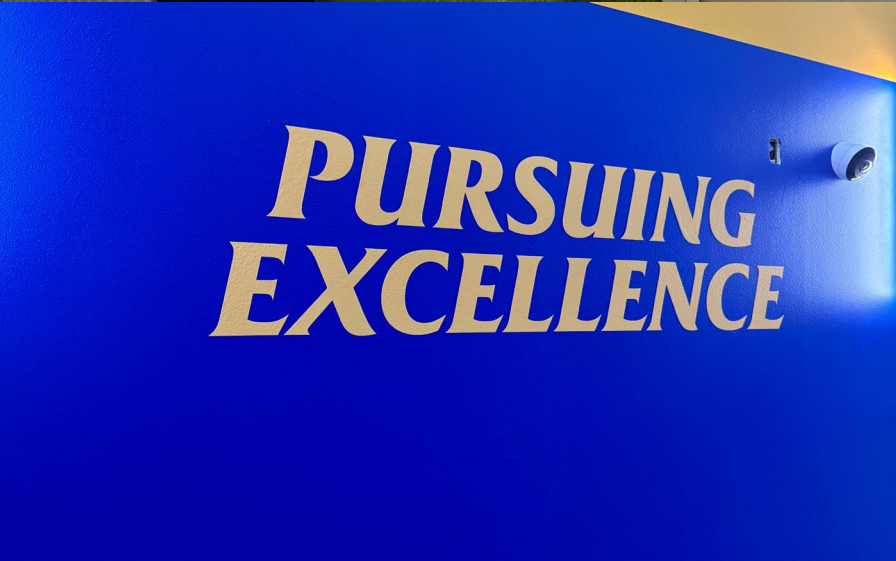



Milestones & Metrics:

Manhours this reporting period:	1472
Total Onsite Manhours to Date:	113,704
Volume of Concrete Placed to Date:	6,620 CY
Rain Events since last report:	7
Rainfall to Date in May:	1.81"
Total Rainfall Year-to date:	15.71"
Tons of Asphalt Placed	300



Looking Ahead: Over the next 3-Weeks

Earthwork/Civil:

- Weller & Society Drives and parking lot paving – June 8th target for completion
- Irrigation and landscaping completion.
- Fire Lane and Parking lot striping

Athletic & Human Performance Buildings:

- Final finishes and equipment installations.
- Signage installations
- Trophy case and PING exhibit installation

Lobby Building & Pump House:

- Punchlist finishes and equipment installations.

Dome & Track

- Punchlist finishes and equipment installations

Pump House

- Fire Protection / Fire Alarms commissioning & Final Inspection.
- Final signage installations



Project Completion is expected in June.
This will be our last Progress Report.
