
LeTourneau University
Christian Polytechnic University Center

Construction Progress Report

10.29.26

Report Summary:

- Building Foundations 100% complete
- Concrete paving in progress
- Site grading and road base in progress
- Exterior electrical/telecommunication in progress
- Level 1 & 2 Structural Steel in progress

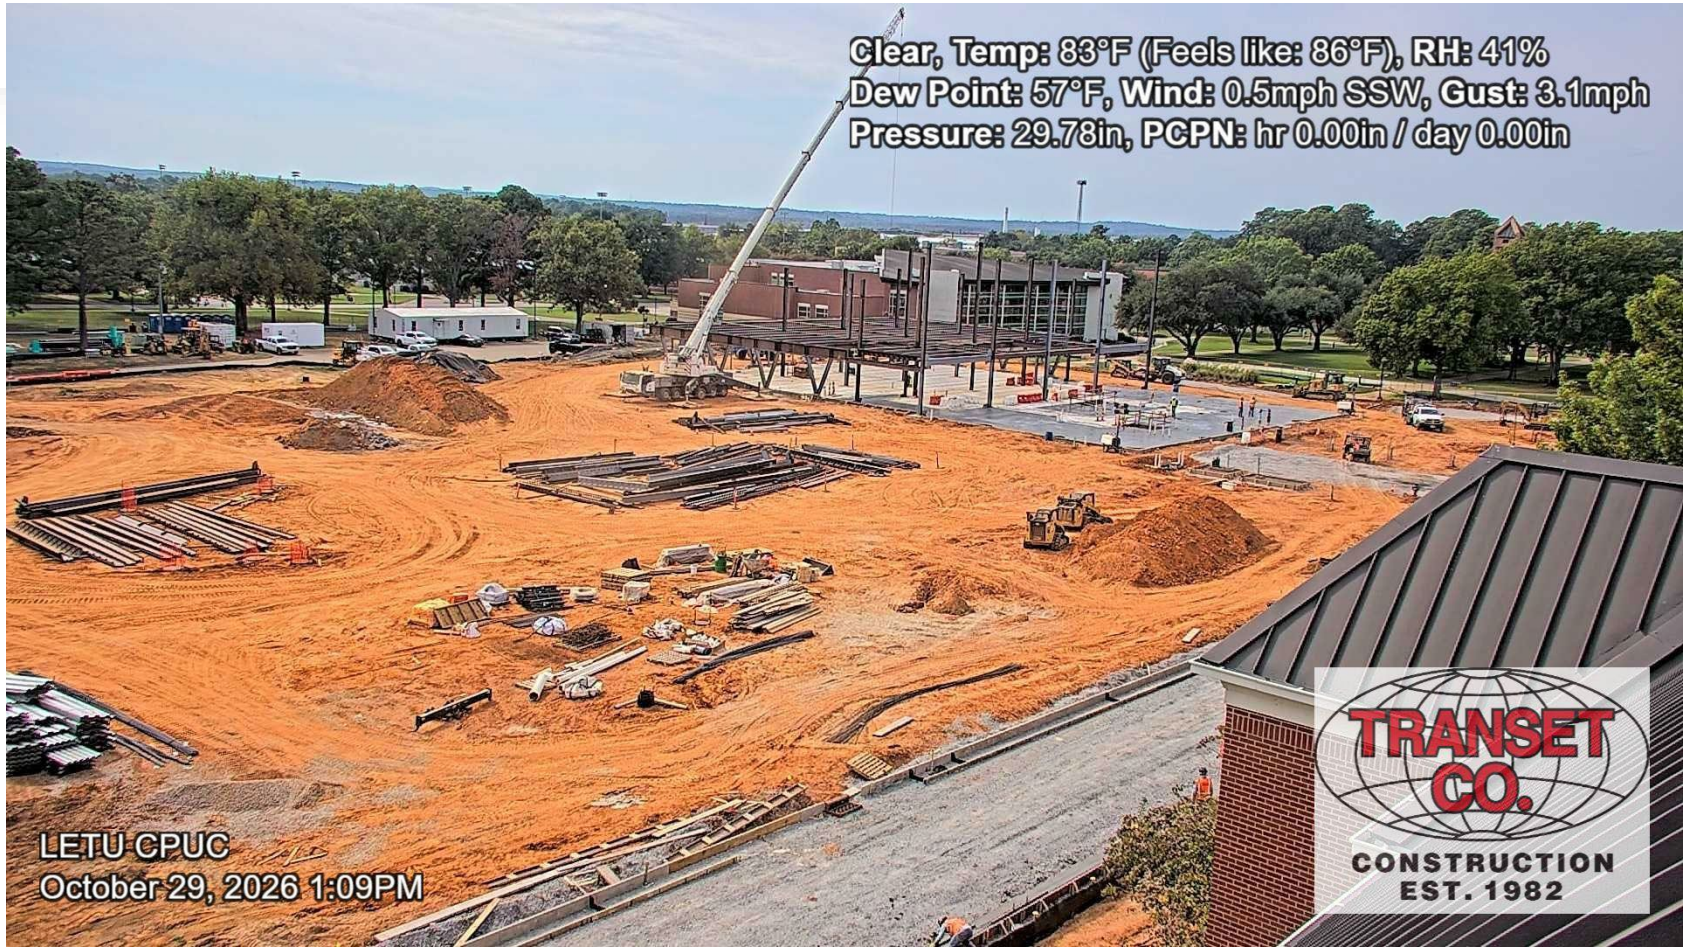

Progress Report:

Earthwork/Civil:

- Stormwater lines: Full scope is ~75% complete
  - Storm Sewer installation will resume after Steel is Erected
- General grading 85% complete
- West water line 95% complete awaiting City Inspections
- NW fire lane 40% complete

Structural:

- Column footers are 100% complete
- Grade beam is 100% complete
- Slab on Grade is 100% complete – North slab poured 10/29/2026
- South tower 1&2 floor structural steel erection 70% complete

Electrical/Telecommunication:

- Temporary power installation 70% complete



Milestones & Metrics:

- Total Onsite Manhours to Date: 13,215.5
- Truckloads of Spoils Hauled offsite: 1,136 trips
- Total Volume of Earth Moved out: 15,757 CY
- Total tonnage of rock received: 1,522 tons
- Volume of Concrete Placed to Date: 1314 CY
- Rain Events since last report: 0
- Rainfall for October: .48”
- Total Rainfall Year-to date: 24.39”











Looking Ahead:
Over the next 3-Weeks

- Complete curb and gutter at North fire lane
- Electrical Primary Service planned & work started
- Complete road base for North and West fire lanes
- Continue pour out of West fire lane
- Delivery of Structural Steel for Level 3
- Begin Steel Erection of Levels 1 & 2 at North tower

Additional Information is available on Procore



Project Completion is expected in July of 2028.
